



## CITY OF DORAL Office of the City Manager Letter to Council

LTC No.: 001-2023

To: The Honorable Mayor and Members of the City Council

From: Barbara Hernandez, City Manager

Date: January 23, 2023

Subject: **Roadway Closure of NW 97<sup>th</sup> Ave (NW 58<sup>th</sup> St - NW 66<sup>th</sup> St)**


The purpose of this Letter to Council (LTC) is to provide the Mayor and City Councilmembers information on the planned roadway closure of NW 97<sup>th</sup> Avenue from NW 58<sup>th</sup> Street to NW 66<sup>th</sup> Street. Miami-Dade County (MDC) is proceeding with their planned roadway closure of NW 97<sup>th</sup> Avenue from NW 58<sup>th</sup> Street to NW 66<sup>th</sup> Street starting Monday, January 23, 2023. The closure will last for 3 weeks (weather permitting). Please know that this closure was originally programmed to commence on Monday, January 9, 2023. However, at the request of the City, the start was asked to be pushed back to Monday, January 23, 2023 as to not coincide with the return of school start date and provide time for traffic patterns to normalize after the holidays. Attached please find a copy of the approved Maintenance of Traffic (MOT) plan.

This road closure is part of the roadway improvements to NW 97 Avenue from NW 58 Street to NW 70 Street (MDC Project No. 20200117). The work consists of widening the existing roadway from a (2) lane to four (4) lane divided roadway, sidewalks, curb and gutter, bicycle facilities, continuous storm drainage system, signalization, pavement markings and signing, and street lighting.

If you have any questions on this matter, please do not hesitate to contact the City Manager's Office or Carlos Arroyo, Public Works Director.

c: Carlos Arroyo, Public Works Director



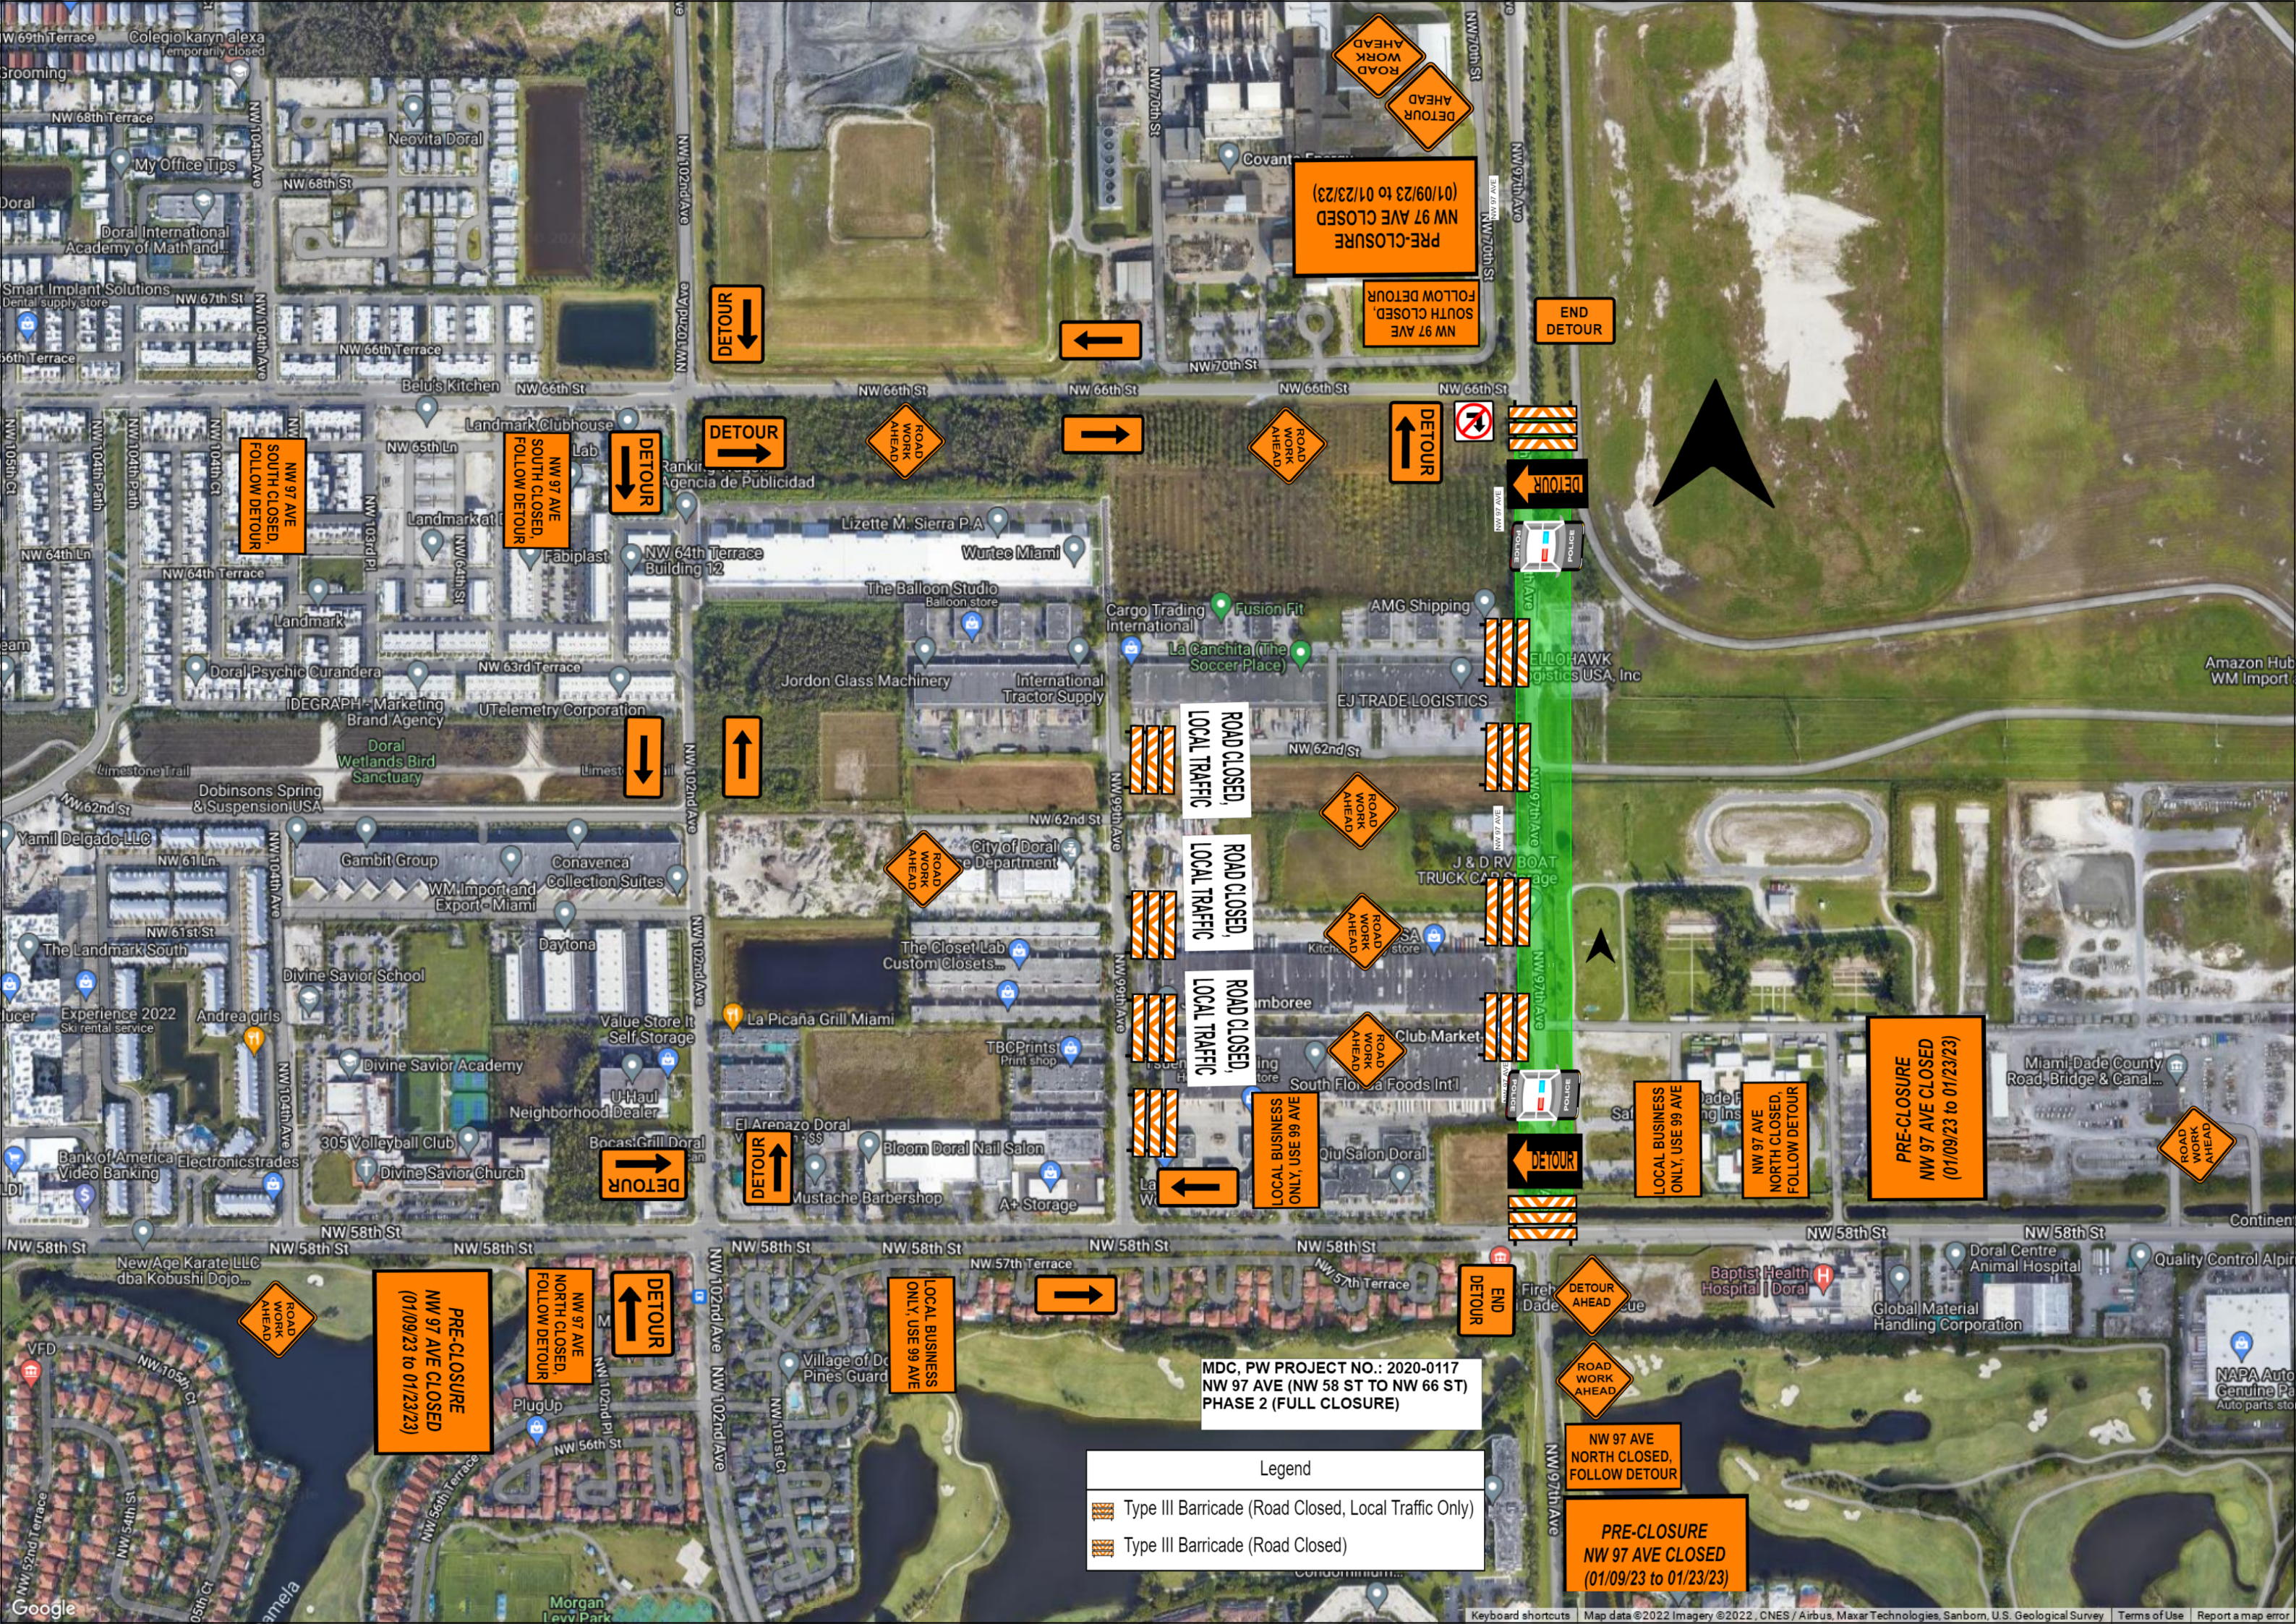

PRE-CLOSURE  
NW 97 AVE CLOSED  
(01/09/23 to 01/23/23)

NW 97 AVE  
SOUTH CLOSED,  
FOLLOW DETOUR

END  
DETOUR

DETOUR

↑

→

DETOUR

DETOUR

NW 97 AVE  
SOUTH CLOSED,  
FOLLOW DETOUR

NW 97 AVE  
SOUTH CLOSED,  
FOLLOW DETOUR

DETOUR

DETOUR

ROAD  
WORK  
AHEAD

ROAD  
WORK  
AHEAD

↓

↑

ROAD CLOSED,  
LOCAL TRAFFIC

ROAD CLOSED,  
LOCAL TRAFFIC

ROAD CLOSED,  
LOCAL TRAFFIC

ROAD  
WORK  
AHEAD

ROAD  
WORK  
AHEAD

ROAD  
WORK  
AHEAD

LOCAL BUSINESS  
ONLY, USE 99 AVE

LOCAL BUSINESS  
ONLY, USE 99 AVE

NW 97 AVE  
NORTH CLOSED,  
FOLLOW DETOUR

PRE-CLOSURE  
NW 97 AVE CLOSED  
(01/09/23 to 01/23/23)

ROAD  
WORK  
AHEAD

ROAD  
WORK  
AHEAD

PRE-CLOSURE  
NW 97 AVE CLOSED  
(01/09/23 to 01/23/23)

NW 97 AVE  
NORTH CLOSED,  
FOLLOW DETOUR

DETOUR

LOCAL BUSINESS  
ONLY, USE 99 AVE

→

MDC, PW PROJECT NO.: 2020-0117  
NW 97 AVE (NW 58 ST TO NW 66 ST)  
PHASE 2 (FULL CLOSURE)

Legend

- Type III Barricade (Road Closed, Local Traffic Only)
- Type III Barricade (Road Closed)

NW 97 AVE  
NORTH CLOSED,  
FOLLOW DETOUR

PRE-CLOSURE  
NW 97 AVE CLOSED  
(01/09/23 to 01/23/23)





**FDOT** This Certifies that  
**XAVIER SALVAT**  
Has Completed a Florida Department of Transportation Approved  
Temporary Traffic Control (TTC) Advanced (Refresher) Course.  
Date Expires: 02/09/2026 Certificate # 81463  
Instructor: Ronald C. Appel FDOT Provider # 434

A&SW Consultants, Inc.  
Phone: 386-788-9899  
5545 Benchmark Lane  
Sanford, FL 32773  
www.FloridaMOT.com  
nicolle@aswconsultants.com

**A&SW**  
Consultants, Inc.


MDC, PW PROJECT NO.: 2020-0117  
NW 97 AVE (NW 58 ST TO NW 66 ST)  
PHASE 2 (FULL CLOSURE)

**Legend**


- Type III Barricade (Road Closed, Local Traffic Only)
- Type III Barricade (Road Closed)

**PRE-CLOSURE**  
NW 97 AVE CLOSED  
(01/09/23 to 01/23/23)



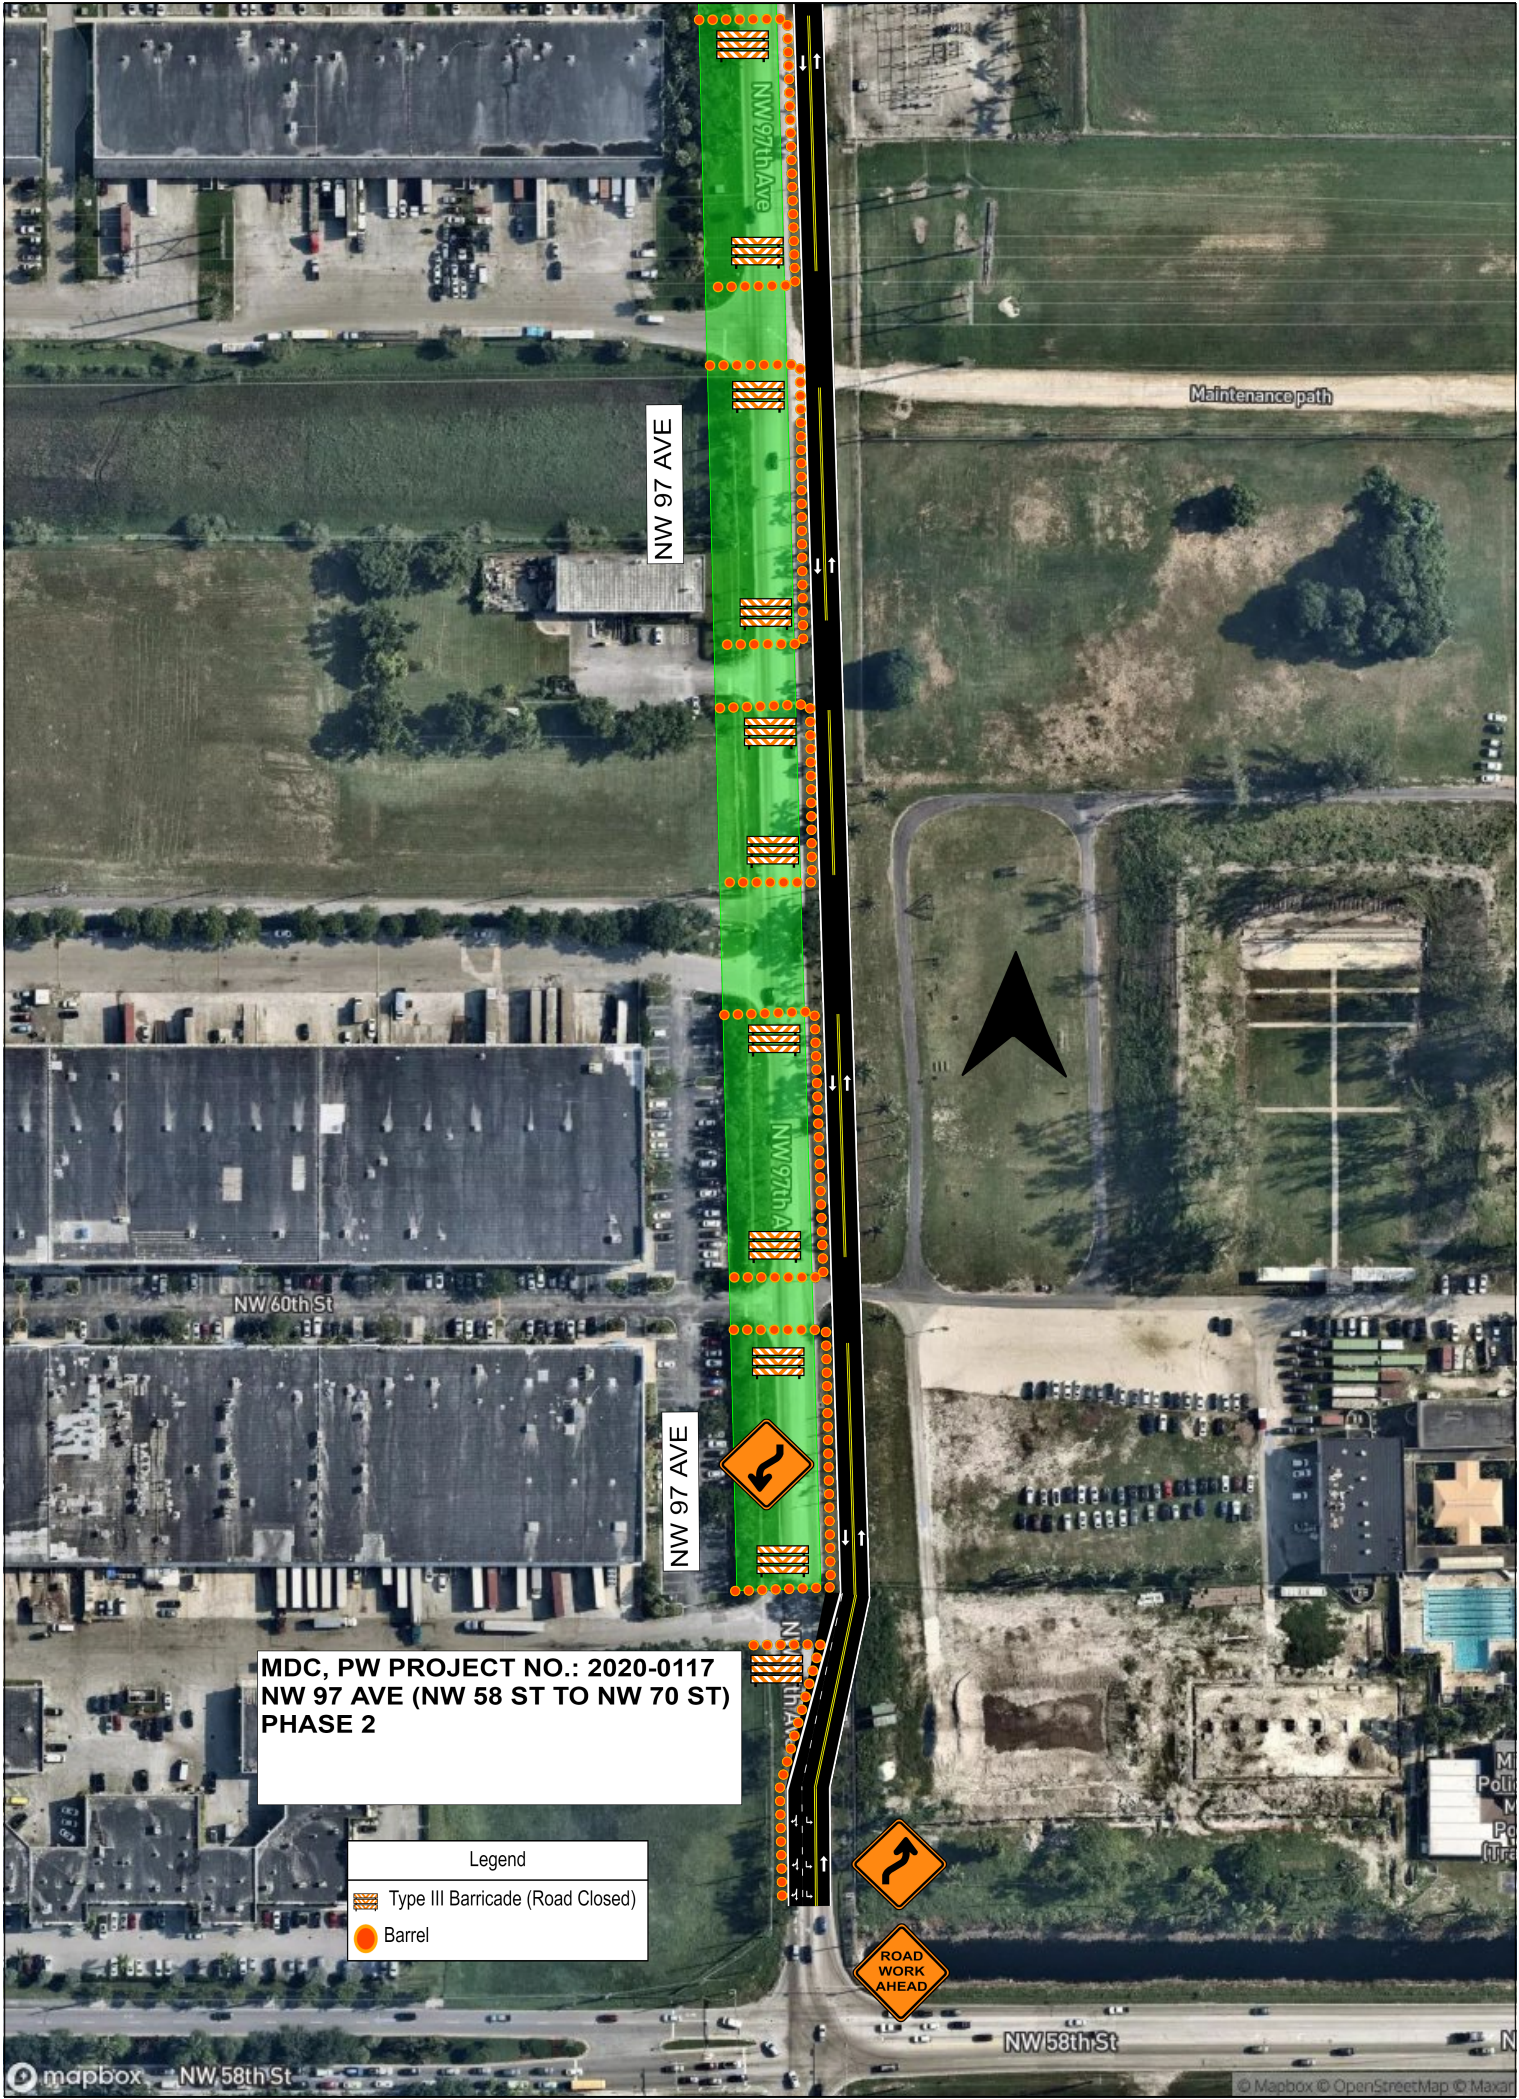



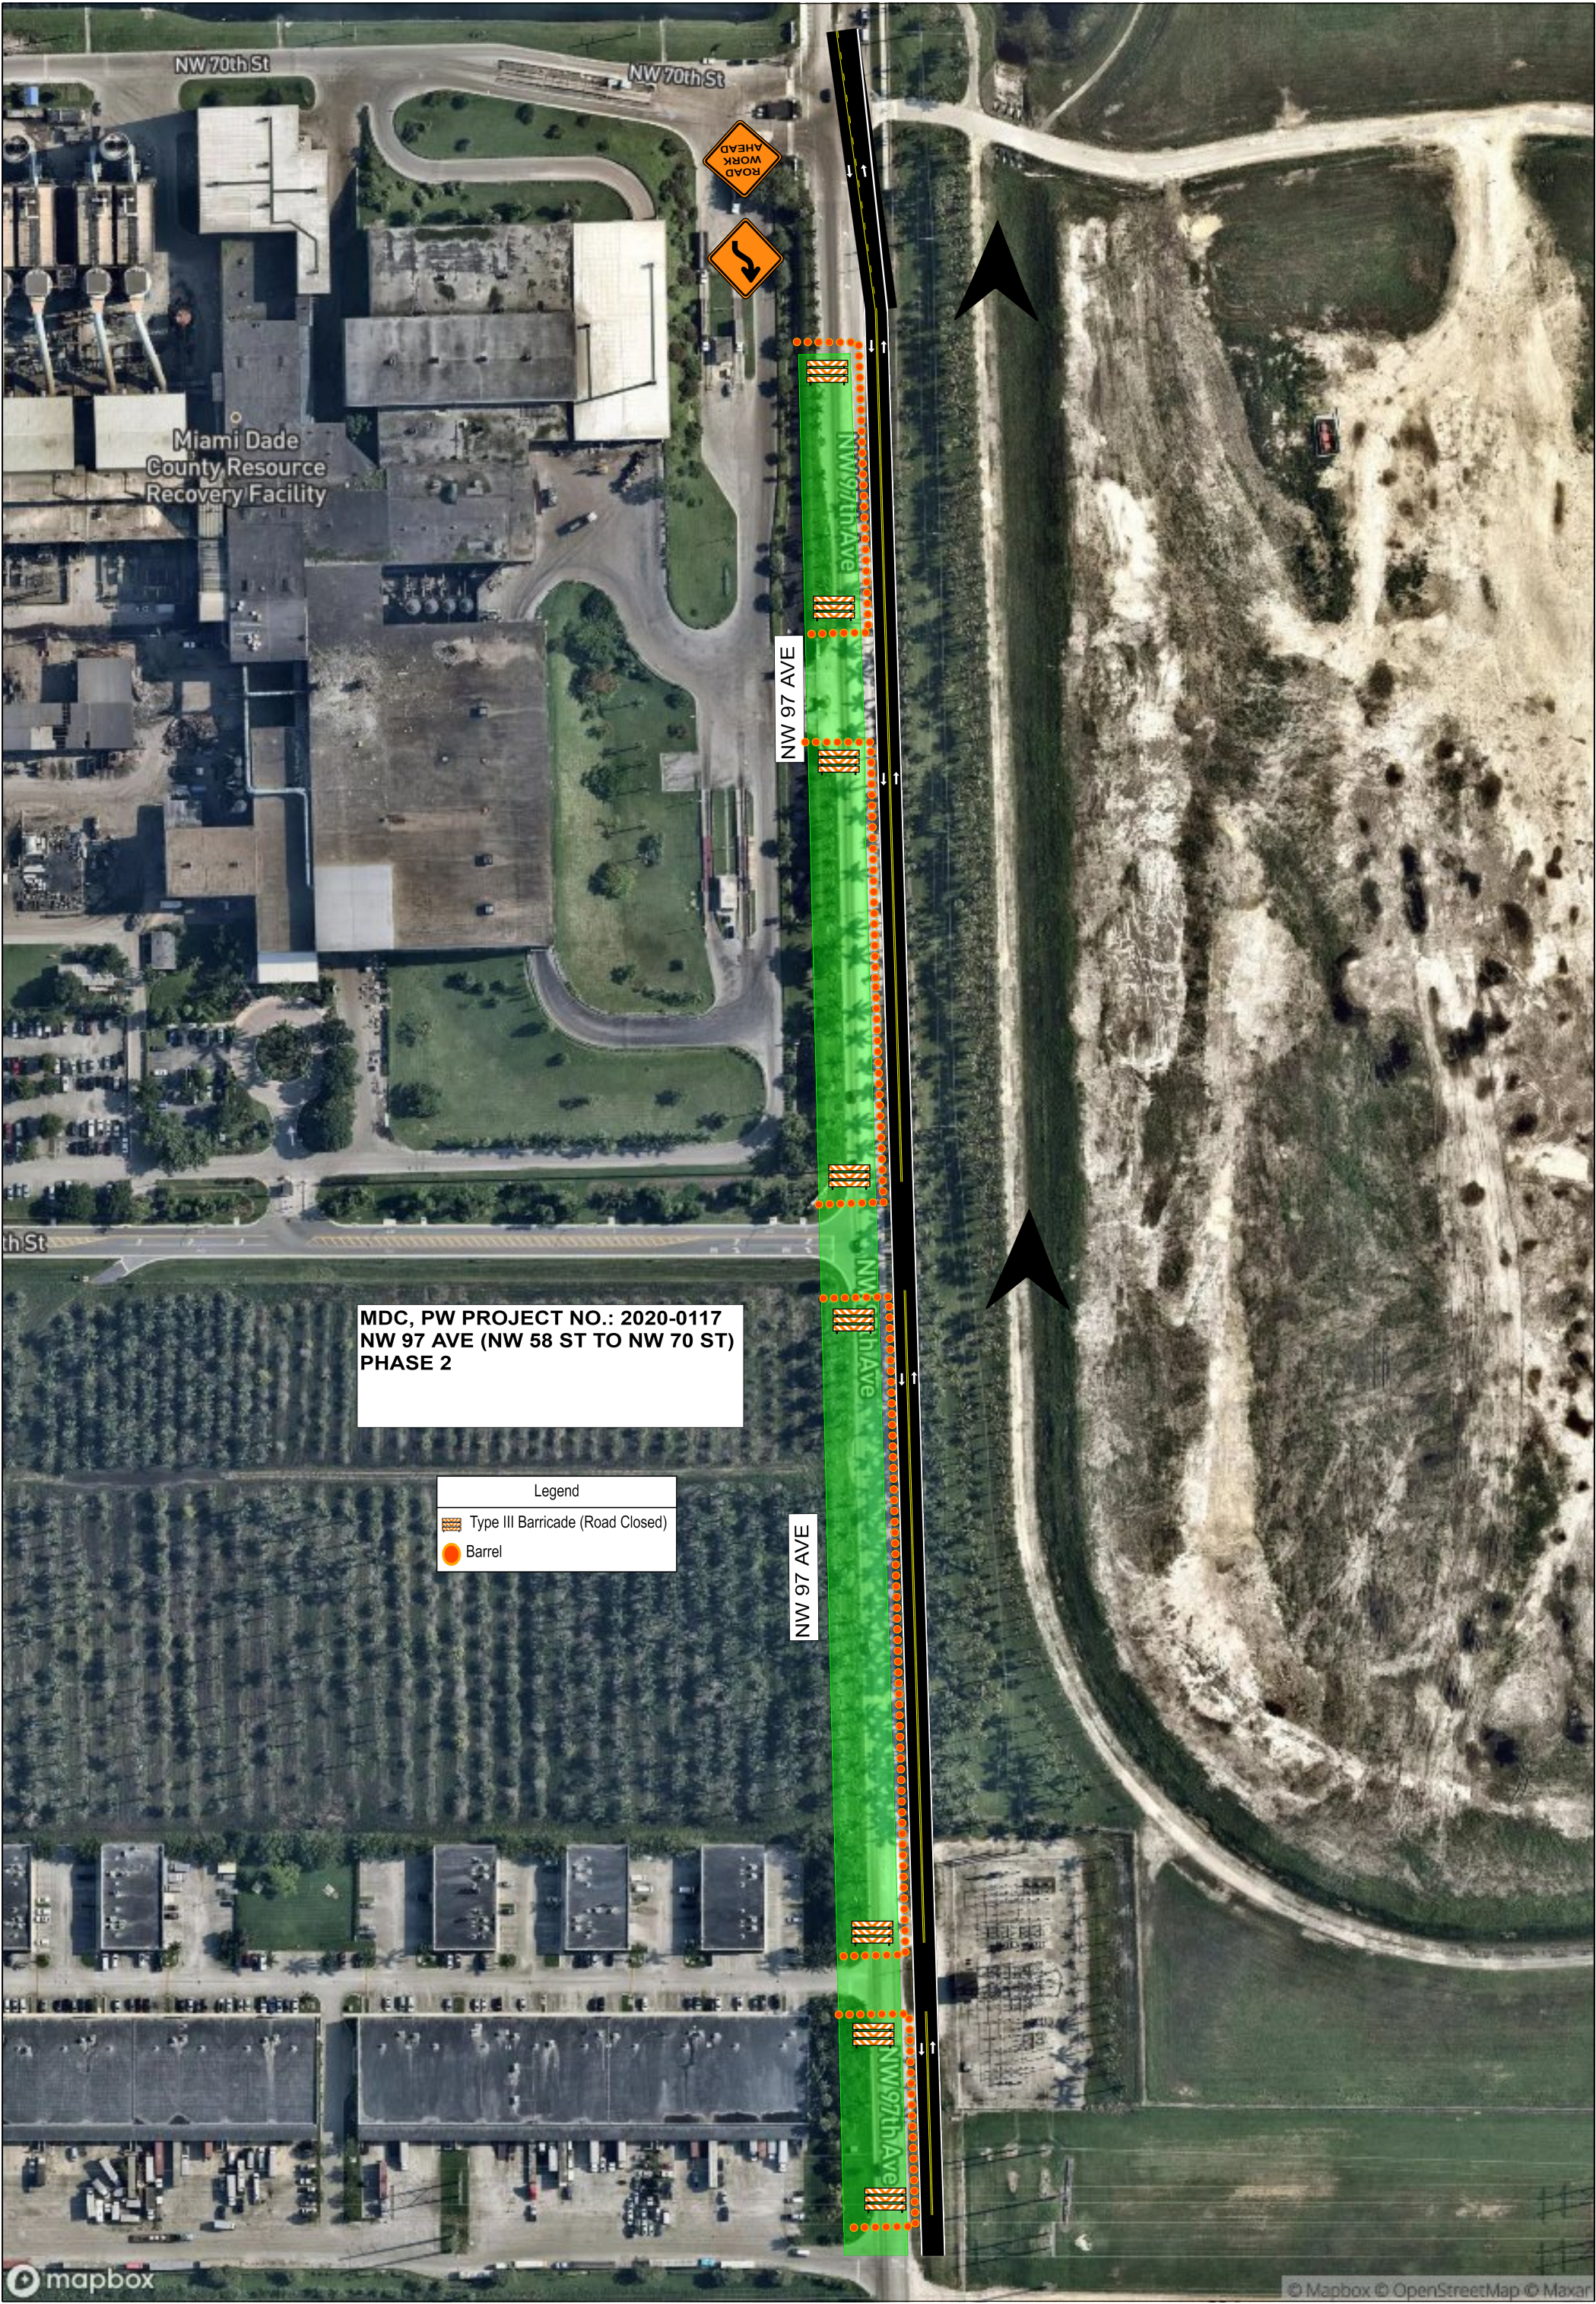

NW 70th St

NW 70th St

Miami Dade  
County Resource  
Recovery Facility



NW 97 AVE

NW 97 AVE

NW 97th Ave

NW 97th Ave

NW 97th Ave

MDC, PW PROJECT NO.: 2020-0117  
NW 97 AVE (NW 58 ST TO NW 70 ST)  
PHASE 2

Legend

- Type III Barricade (Road Closed)
- Barrel





8175 West 32nd Avenue, Suite #1, Hialeah, Florida 33018  
Phone: (305) 828-2050 Fax: (305) 820-0905

Thursday, November 17 2022

Transmitted Via Fax: (786) 469-5580

Miami Dade County, Public Works Department  
111 NW 1<sup>st</sup> Street  
Miami, FL 33128

Attn: **Mr. Eulois Cleckley**  
Director  
Department of Transportation and Public Works

Re: Project Name: NW 97 Ave from NW 58 Street to NW 70 Street  
Financial Project No's: NA  
Federal Job Number: NA  
Contract No.: 2020-0117  
County: Miami-Dade, Florida

**LET 399-02 MDC 2020-0017 NW 97 AVE full Closure from NW 58 ST to NW 66 ST (REVISED)**

With respect to the above referenced Project, HCI is respectfully requesting approval to implement a complete road closure on NW 97 Avenue from NW 58 Street to NW 66 Street to expeditiously bring the existing grade to match the new roadway proposed grade. This will include the expedited construction of side street connectors, business turnouts and property harmonization's. A comprehensive detour plan will be implemented including static & variable message signage instructing motorists to access local business on the west side of NW 97<sup>th</sup> Avenue through NW 99<sup>th</sup> Avenue which is a parallel adjacent corridor for which these businesses have access to.

Horizon Contractors, Inc. in connection with Miami Dade County will engage in a public information campaign to ensure all local businesses and stake holders are well informed of the proposed timelines, alternate routes and work to be performed during this closure.

This construction work has been intentionally scheduled for after the busy holiday season to minimize impacts. At this time the full 24-hour road closure is scheduled to commence on Monday, January 09, 2023 with a tentative opening scheduled for Monday, January 30, 2023.

A full closure is imperative to perform a safe and expeditious traffic switch while maintain access to local stakeholders and ensuring the safety of the traveling public.

Sincerely,  
**Horizon Contractors, Inc.**

Xavier Salvat, P.E.  
Project Manager

CC: Josenrique Cueto, P.E. County Engineer/Deputy Director  
Yamilet Senespleda, P.E., Chief of Traffic Engineering Division and County Traffic Engineer
